

SAND PLANET

PLANET

USER GUIDE

Site documents, procurement, and project cost control — everything your team used to keep in Excel, now in one place.

DOCUMENT	REVISION	PREPARED BY	DATE
PLANET-UG-01	R2	Shahiq	10 / 07 / 26

For Sand Planet Pvt Ltd · internal

The idea in one paragraph

Every form you used to keep in Excel now lives in one place. You fill it in, Planet numbers it, files it in the right register, and produces the PDF you send to the client. The registers maintain themselves.


But the real point is underneath: every material bought, every payment made, every hour worked flows into one number per project — what it has cost so far, against what you are being paid. Nothing gets lost, nothing gets typed twice, and at any moment anyone with the right to know can see exactly where a project stands.

What's in this guide

Signing in & your dashboard	3
How every document works	4
The site documents — DPR, TWS, DMA, IR, MAR, MR, GRN, PYR	5
Head Office documents — PR, LM	9
The item catalogue & registers	10
Petty cash	11
Timesheets and payroll	12
How a payment travels	13
Projects and cost	14
International procurement (later phase)	15

Signing in & your dashboard

Your account decides what you see. Sign in and you land straight on your own dashboard — no menus to hunt, no site to choose. Site staff see only their island. Head Office sees all of them. Your Project Manager sees every site they run. Accounts are created by the Administrator; there is no self-registration, and passwords are stored securely on the server.

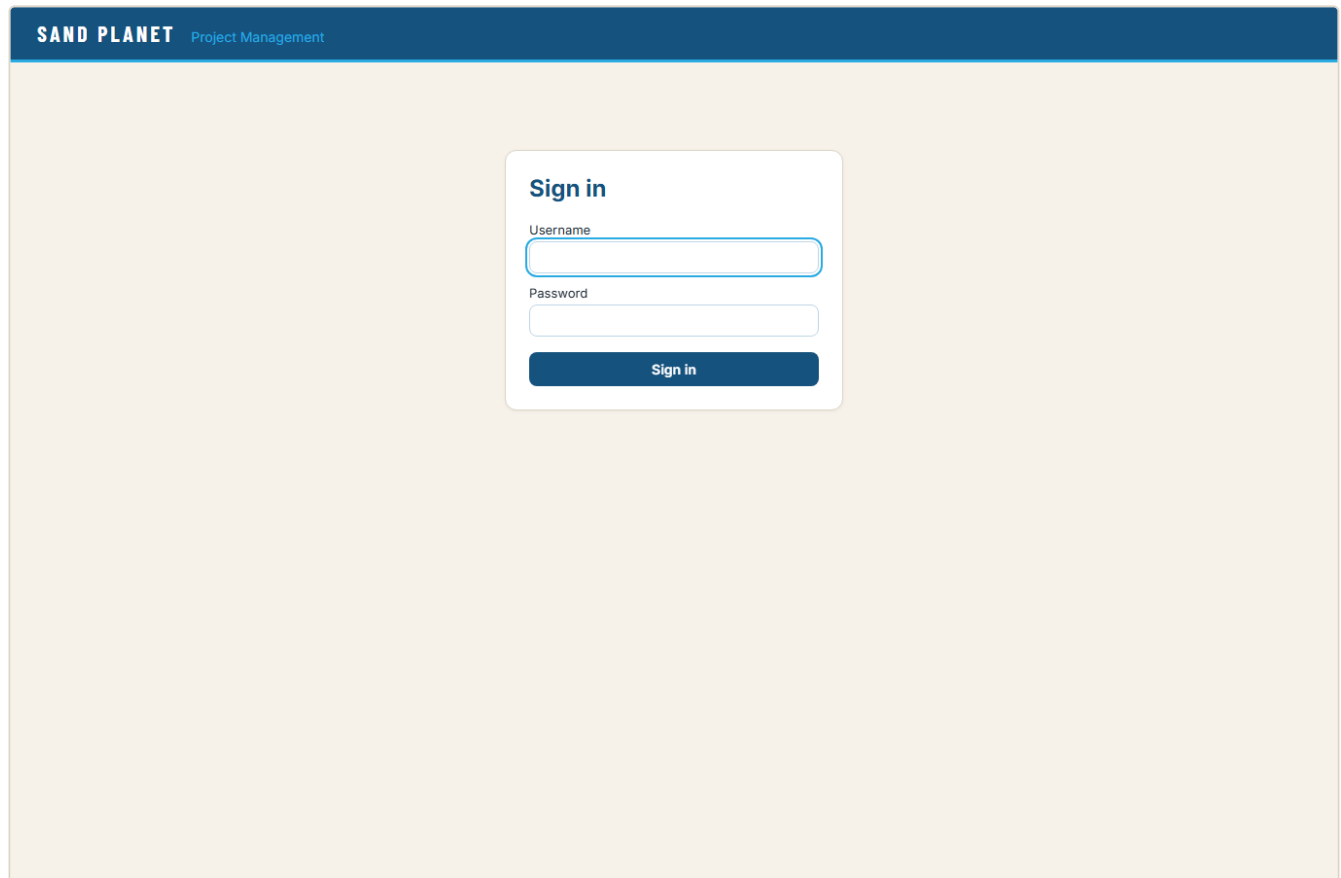


Signing in — your role decides where you land and what you can do.

On your phone. Planet works in a phone browser and can be added to your home screen. Take DPR photos straight from the camera; drafts are held safely if the signal drops and sync when you're back online — don't retype anything.


Your dashboard answers one question: what needs me today?

Your obligations sit at the top. Below them, the things waiting on you — most urgent first, each saying what's wrong, how old it is, and the one button that deals with it. Below that, the numbers, each with its meaning attached: not "3 MRs" but "3 MRs open — oldest 6 days."

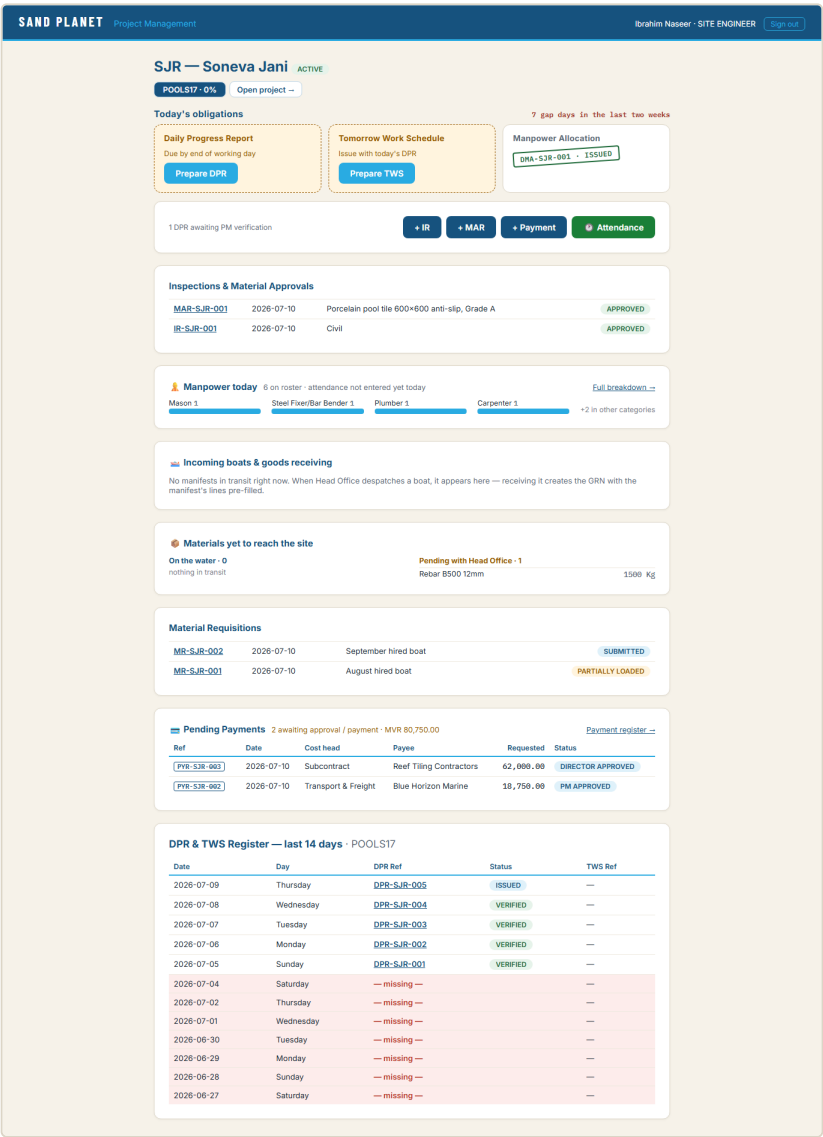


The site dashboard — today's DPR, TWS and manpower as stamp tiles, then everything waiting on the site.


The same idea, shaped for each role

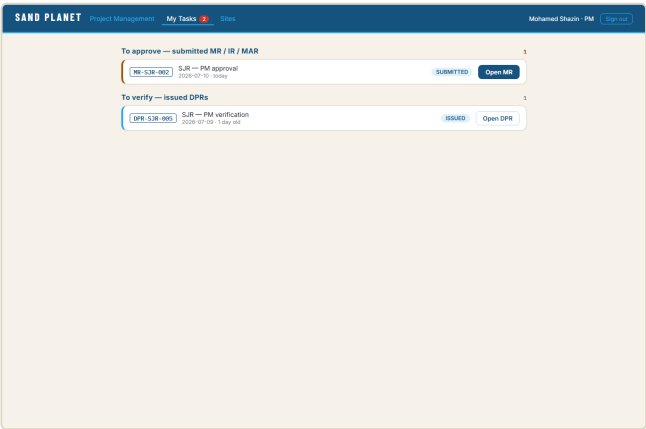


Project Manager — every approval across their sites in one queue.

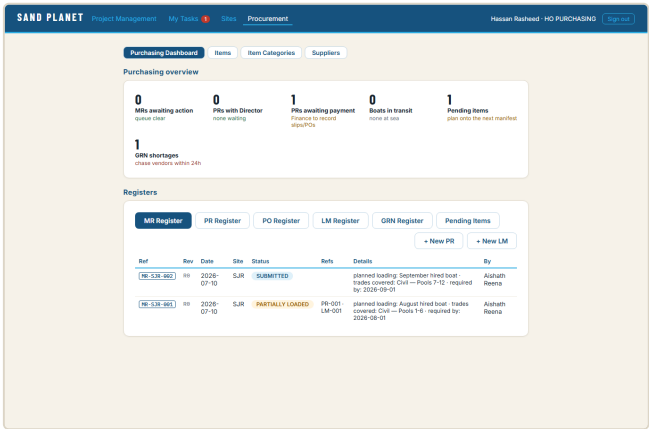

Head Office Purchasing — MRs to process, the boat board, registers.

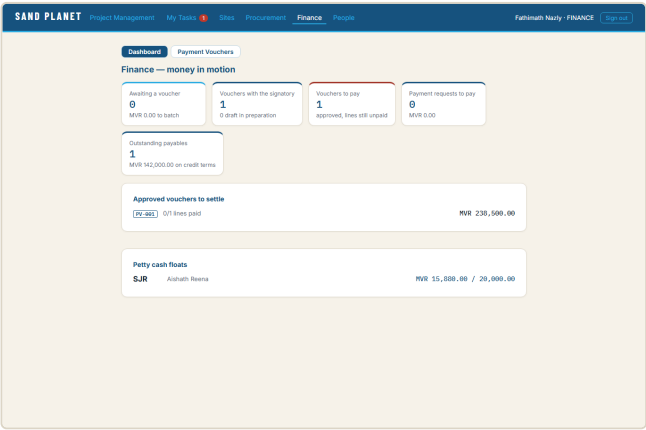

Finance — authorised payments awaiting disbursement, committed vs paid.

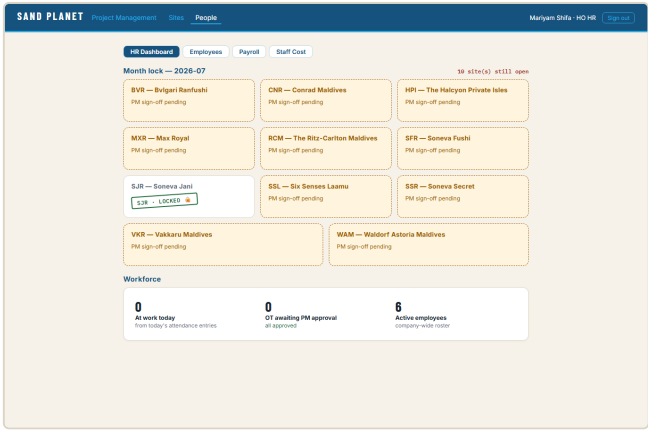

HR & Payroll — the month-lock board and permit expiries.

How every document works

There are thirteen document types. They all behave the same way, so learn it once.

- 1 **Create.** Pick the type, fill it in. Your site is already filled in and locked — you cannot file paperwork under another island. The reference (*DPR-SJR-001*) is issued by Planet, in order, with no gaps.
- 2 **Save as draft** as often as you like. Nothing is final until you issue it.
- 3 **Submit or issue.** Some documents need approval first. Once issued, the document locks — it is the official record.
- 4 **The PDF generates automatically**, on company letterhead, matching your old Excel layout. That is what goes to the client or vendor.
- 5 **The register updates itself.** You never maintain a register again.

1 · You fill in the form on screen...

2 · ...Planet issues, numbers and stamps it...



SANDPLANET

DAILY PROGRESS REPORT

DPR No.	DPR-SJR-001	Date / Day	05.07.2026 — Sunday		
Client	Soneva Jani Resort	Consultant	Atoll Consult Pvt Ltd		
Project / Site	Soneva Jani	Site Code	SJR		
Working Hours		Weather AM	Sunny	Weather PM	Cloudy
If Rained: From / To		Rain Duration (hrs)		Work Time Lost (hrs)	

1. WORK DONE TODAY

No.	Activity	Location / Area / Villa	Today %	To-date %	Remarks
POOLS17 — Proposed Construction of 17 Swimming Pools					
1	PROPOSED CONSTRUCTION OF 17 NOS SWIMMING POOLS	Pool 3	8%	35%	On programme

2. MANPOWER

Staff		Trades / Labour	
Project Manager	-	Mason	4
Site Engineer	1	Carpenter	2
MEP Engineer	-	Steel Fixer/Bar Bender	3
QS/QC	-	Welder	-
Supervisor	-	Plumber	-
Foreman	1	Electrician	-
Site Admin/Storekeeper	-	Painter/Tiler	-
		Skilled Labour	-
		Unskilled Labour	-
		Driver/Kapli/Cleaner	-
TOTAL MANPOWER AT SITE			11

3. MACHINERY & EQUIPMENT IN USE

Item	Nos	Remarks (working / idle / breakdown)
Concrete mixer	2	
Poker vibrator	3	

4. KEY MATERIALS AT SITE

Material	Unit	Opening Stock	Received Today	Consumed Today	Balance	Remarks
Cement OPC 50kg bag	Bag	120	280	60	340	
Rebar B500 12mm	Kg	500	3960	800	3660	

Sand Planet Pvt Ltd · TIN 1052866GST501 | DPR | <http://sandplanet.mv>
Ma. Maaraadha aage | Maldives

3 · ...and produces the letterhead PDF that goes to the client.

Made a mistake after issuing? You don't edit — you revise. MARs and MRs keep their number and step a revision (R0 → R1), with changed lines flagged. A rejected IR returns as a new IR quoting the old one. Anything else can be voided with a reason, and the register keeps the record. **Approval stamps** print the approver's name, role and exact time on the PDF — that is the digital signature.

The site documents

DPR — Daily Progress Report

Weather, rain and time lost, work done with progress percentages, manpower by trade, machinery, key material stock, matters affecting progress, visitors, safety. At least four captioned photos, or Planet won't let you issue it. Goes to the client every working day — issue it without waiting for your PM; the PM verifies afterwards.

TWS — Tomorrow Work Schedule

Goes out with the DPR before the day ends: planned activities, planned manpower, and what you need from the client tomorrow — buggy, villa access, power isolation.



TOMORROW WORK SCHEDULE

Doc No.	TWS-SJR-001	Date	11.07.2026
Project / Site	Soneva Jani (SJR)	Client	Soneva Jani Resort
Consultant	Atoll Consult Pvt Ltd		
Schedule For	11/07/26	Issued On	10/07/26
Working Hours			

1. Planned Activities

No.	Planned Activity	Project	Location/Area/Villa	Trade	Remarks
1	Wall concreting Pool 3	POOLS17	Pool 3	Mason/Tiler	
2	Rebar fixing Pool 4	POOLS17	Pool 4	Steel Fixer/Welder	

2. Planned Manpower — total 0

Group	Category	Count

3. Access / Support Required from Client

Buggy for material movement; villa access 08:00

Prepared By — Site Engineer

Ibrahim Naseer — SITE_ENGINEER —
10/07/26 08:42 — approved electronically via
Sand Planet Project Management App

Acknowledged By — Client Representative

Sand Planet Pvt Ltd · TIN 1052866GST501 | TWS | <http://sandplanet.mv>
 Ma, Maaraadha aage | Maldives

The Tomorrow Work Schedule as issued to the client.

DMA — Daily Manpower Allocation · internal

Each morning the site turns yesterday's TWS into a crew plan: who works where, on which task, under which project. The Site Engineer drafts it and the PM issues it. It is an internal control document — it is not sent to the client — and it feeds the "Manpower today" figures on the dashboard, flagging idle crew when attendance outruns allocation.



SANDPLANET

DAILY MANPOWER ALLOCATION

Doc No.	DMA-SJR-001	Date	10.07.2026	
Project / Site	Soneva Jani (SJR)	Client	Soneva Jani Resort	
Consultant	Atoll Consult Pvt Ltd			
Allocation For	10/07/26	Based on TWS	—	
Working Hours				

1. Task Allocation

No.	Task	Project	Location/Area	Category	Workers	Remarks
1	Wall concreting — Pool 3	POOLS17	Pool 3	Mason	6	
2	Rebar fixing — Pool 4	POOLS17	Pool 4	Steel Fixer	5	
3	Material unloading (dhoni)	General	Jetty	Labourer	6	General

2. Manpower at Work — total 17

Category	Workers
Labourer	6
Mason	6
Steel Fixer	5

Allocated By — Project Manager

Mohamed Shazin — PM — 10/07/26 08:42 — approved electronically via Sand Planet Project Management App

Sand Planet Pvt Ltd · TIN 1052866GST501 | DMA | <http://sandplanet.mv>
 Ma. Maaraadha aage | Maldives

The Daily Manpower Allocation — an internal record of who is on what today.

IR — Inspection Request

Submit at least 24 hours ahead. Your PM approves before it goes to the client. Record the client's result — approved, approved with comments, or rejected. Comments close out in Part C with evidence; rejected work returns as a new IR.

SAND PLANET

Project Management

Ibrahim Naseer · SITE ENGINEER

Sign out

IR-SJR-001

RO

APPROVED

Close

Inspection Request · Soneva Jani · 2026-07-10 · prepared by Ibrahim Naseer

PDF — IR-SJR-001-RO-issue.pdf

PDF — IR-SJR-001-RO-result.pdf

APPROVED — Approved to proceed with concreting.

J. Perera · Resident Engineer

Details

discipline

Civil

location

Pool 3

requested date

2026-07-12

requested time

10:00

work description

Pool 3 wall reinforcement — pre-concrete inspection

work after

Wall concreting

ref drawings

ST-204, ST-205

enclosed

Yes

Workflow trail

SUBMIT — Ibrahim Naseer (SITE ENGINEER) — 10/07/2026, 13:42:22

APPROVE — Mohamed Shazin (PM) — 10/07/2026, 13:42:22

ISSUE — Ibrahim Naseer (SITE ENGINEER) — 10/07/2026, 13:42:22

RESULT_RECORDED (APPROVED) — Ibrahim Naseer (SITE ENGINEER) — 10/07/2026, 13:42:23 — "Approved to proceed with concreting."

An issued IR with the client result and full workflow trail recorded.

MAR — Material Approval Request

Getting a material approved before ordering: description, manufacturer, origin, specification and drawing references, attachments. The PM approves, then it goes to the client. Never order material before written approval.

SAND PLANET

Project Management

Ibrahim Naseer · SITE ENGINEER

Sign out

MAR-SJR-001

RO

APPROVED

Close

Material Approval Request · Soneva Jani · 2026-07-10 · prepared by Ibrahim Naseer

PDF — MAR-SJR-001-R0-issue.pdf

PDF — MAR-SJR-001-R0-result.pdf

APPROVED

J. Perera · Resident Engineer · 2026-07-10

Details

material description

Porcelain pool tile 600×600 anti-slip, Grade A

manufacturer

RAK Ceramics

origin

UAE

spec ref

Finishes spec §4.2

confirms spec

Yes

Enclosures: Sample, Catalogue

Workflow trail

SUBMIT — Ibrahim Naseer (SITE ENGINEER) — 10/07/2026, 13:42:23

APPROVE — Mohamed Shazin (PM) — 10/07/2026, 13:42:23

ISSUE — Ibrahim Naseer (SITE ENGINEER) — 10/07/2026, 13:42:23

RESULT_RECORDED (APPROVED) — Ibrahim Naseer (SITE ENGINEER) — 10/07/2026, 13:42:24

A Material Approval Request — approved by the client before ordering.

MR — Material Requisition

The only way a site asks for materials. One MR per loading, all trades. Pick items from the catalogue; enter what you need and what's physically on site, and Planet calculates what to order. Reach Head Office at least seven working days before the boat. PM approval is mandatory. A new requirement before loading? Amend the same MR — don't raise a second one.

SAND PLANET
Project Management

Aishath Reena · SITE ADMIN
Sign out

MR-SJR-001
R0
PARTIALLY LOADED
Close

Material Requisition · Soneva Jani · 2026-07-10 · prepared by Aishath Reena
References: PR-001 · LM-001

Amend (new revision)
Close
PDF — MR-SJR-001-R0-sent.pdf

planned loading August hired boat
trades covered Civil — Pools 1-6
required by 2026-08-01
stock attested true

Items

Description	Unit	Required	Stock	To Order	Priority	Remarks
Cement OPC 50kg bag	Bag	400.00	120.00	280.00	NORMAL	Civil
Rebar B500 12mm	Kg	6000.00	500.00	5500.00	NORMAL	Civil
Hollow block 8"	Nos	2500.00	0.00	2500.00	URGENT — Blockwork starts next boat	

Workflow trail

SUBMIT — Aishath Reena (SITE ADMIN) — 10/07/2026, 13:42:25
APPROVE — Mohamed Shazin (PM) — 10/07/2026, 13:42:26
SEND — Aishath Reena (SITE ADMIN) — 10/07/2026, 13:42:26

A Material Requisition — catalogue items, stock on site, quantity to order.

GRN — Goods Received Note

When the boat arrives, choose the manifest and every item loads automatically with the shipped quantities. Count physically, enter what actually arrived, and Planet calculates shortages and flags them red. Report shortages or damage within 24 hours — Planet starts that clock and notifies Head Office.



GOODS RECEIVED NOTE

Doc No.	GRN-SJR-001	Date	10.07.2026
Project / Site	Soneva Jani (SJR)	Client	Soneva Jani Resort
Manifest Ref	LM-001	Vessel/Boat	MV Dhoni 7
Date Received			
References	LM-001		

No.	Item Description	Unit	Qty as per Manifest	Qty Received	Shortage/Excess	Condition/Remarks
1	Cement OPC 50kg bag	Bag	280	280	0	
2	Rebar B500 12mm	Kg	4,000	3,960	-40	40kg short — coil damaged
3	Hollow block 8"	Nos	2,500	2,500	0	

Received/Counted By — Site Admin / Storekeeper	Verified By — Site Engineer / PM
Aishath Reena — SITE_ADMIN — 10/07/26 08:42 — approved electronically via Sand Planet Project Management App	Mohamed Shazin — PM — 10/07/26 08:42 — approved electronically via Sand Planet Project Management App

Sand Planet Pvt Ltd · TIN 1052866GST501 | GRN | <http://sandplanet.mv>
Ma. Maaraadha aage | Maldives

A Goods Received Note — received quantities counted against the manifest.

PYR — Payment Request

For spending that isn't materials: boat hire, subcontractors, equipment rental, permits, repairs. Attach the bill or quotation; if there isn't one, say so and give the reason — above a set amount an attachment or a PM override is required. Then it travels: you → your PM → HO Director → a company signatory → Finance pays.

SAND PLANET

Project Management

Aishath Reena · SITE ADMIN

Sign out

PYR-SJR-001

Payment Request

PAID

Back

Site	SJR		
Payment type	DIRECT		
Cost head	Transport & Freight		
Payee	Island Boat Services		
Method	BANK · 7770000012345 (BML)		
Amount requested	MVR 24,500.00		
Required by	2026-07-18		
Purpose	Boat hire for July materials loading (Male'-Medhufaru)		
Supporting doc	Yes (0 attached)		
Amount paid	MVR 24,500.00		
Payment ref	TRF-30044		

Action	By	When	Comment
SUBMIT	Aishath Reena (SITE_ADMIN)	10/07/2026, 13:42:28	
PM APPROVE	Mohamed Shazin (PM)	10/07/2026, 13:42:28	
DIRECTOR APPROVE	Ahmed Zahir (DIRECTOR)	10/07/2026, 13:42:28	
AUTHORISE	Ali Waheed (SIGNATORY)	10/07/2026, 13:42:28	Authorised on voucher
PAY	Fathimath Nazly (FINANCE)	10/07/2026, 13:42:28	

A paid Payment Request, showing every step from raise to disbursement.

Head Office documents

PR — Procurement Requisition

Raised against MRs: vendors, quotations, terms, amounts. Every local purchase is either cash or credit — never part-paid. On authorisation the purchase order issues on company letterhead.

PR-001 PAYMENT PROCESSING Close

Procurement Requisition - Sonewa Jani - 2026-07-10 - prepared by Hassan Rashad

References: MR-SLR-001 - LM-001

[PDF - PR-001-RO-approved.pdf](#)

requested delivery 2026-07-25

Vendor	Quotation Ref	Terms	PO / Payment Ref	Cash	Credit	Total
Alta Building Supplies	QT-4411	COD	TRF-30021	96,500	0	96,500
Makr Hardware Pvt Ltd	QT-8820	30 days	---	0	142,000	142,000
Untaxed Amount				96,500	142,000	238,500
GST (8%)						19,080
Total incl. GST						MVR 257,580

Quotations & MR coverage

Not quoted: Cement OPC 50kg bag, Rebar 8500 12mm, Hollow block 8"

[View quotations](#)

Workflow trail

SUBMIT - Hassan Rashad (HO_PURCHASING) - 10/07/2026, 13:42:26
 APPROVE - Ahmed Zahr (DIRECTOR) - 10/07/2026, 13:42:26
 AUTHORISE - Ali Rashad (SIGNATORY) - 10/07/2026, 13:42:27 - "Authorized on voucher"
 PAYMENT RECORDED - Fatmawati Nazy (FINANCE) - 10/07/2026, 13:42:27 - "Alta Building Supplies TRF-30021"

The PR — vendors and amounts against the MR.

SANDPLANET **PROCUREMENT REQUISITION**

Doc No	PR-001	Date	10.07.2026
Project / Site	Sonewa Jani (BJR)	Client	Sonewa Jani Resort
Requested Delivery	2026-07-25		
References	MR-SLR-001		

No.	Vendor	Quotation Ref	Terms	PO / Payment Ref	Cash (MVR)	Credit (MVR)	Total (MVR)
1	Alta Building Supplies	QT-4411	COD		96,500		96,500
2	Makr Hardware Pvt Ltd	QT-8820	30 days			142,000	142,000
Untaxed Amount					96,500.00	142,000.00	238,500.00
GST (8%)							19,080.00
Total incl. GST							257,580.00

Prepared By — Purchasing	Approved By — Sr PM / Director / Projects	Finance — Payment / PO issued
Hassan Rashad — HO_PURCHASING — 10/07/26 08:42 — approved electronically via Sand Planet Project Management App	Ahmed Zahr — DIRECTOR — 10/07/26 08:42 — approved electronically via Sand Planet Project Management App	

Sand Planet Pvt Ltd | TIN: 102386227001 | PR | <http://sandplanet.mv>
 Mr. Hassan@sa.sgi13.netlify.com

...and the Purchase Order it produces for the vendor.

LM — Loading Manifest

What's on the boat: vessel, destination, quantities loaded, quantities still pending. Pending items go automatically into the Pending Items Log. The destination site raises its GRN straight from this manifest.

SAND PLANET

Project ManagementMy Tasks1SitesProcurement

Hassan Rasheed · HO PURCHASINGSign out

LM-001R0

RECEIVED WITH SHORTAGE

Close

Loading Manifest · Soneva Jani · 2026-07-10 · prepared by Hassan Rasheed

References: MR-SJR-001 · PR-001 · GRN-SJR-001

PDF — LM-001-R0-departed.pdf

vesselMV Dhoni 7

departure pointMale'

expected arrival2026-07-20

Items

Description	Unit	Loaded	Pending	Remarks
Cement OPC 50kg bag	Bag	280.00	0.00	
Rebar B500 12mm	Kg	4000.00	1500.00	
Hollow block 8"	Nos	2500.00	0.00	

Workflow trail

DEPART — Hassan Rasheed (HO PURCHASING) — 10/07/2026, 13:42:27

A Loading Manifest — loaded and pending quantities per item.

The item catalogue & registers

One company-wide list of materials, each with a fixed description and unit. Build an MR by searching the catalogue and picking items — no more "steel pipe" on one form and "25mm SS316 pipe, 6m" on another. Need something not listed? Type it as free text; it's flagged as a new item and you're never blocked. Head Office reviews it and either matches it to something existing or adds it properly. Because everyone uses the same item, one product can be followed all the way through: requested, purchased, loaded, received.

The screenshot shows the 'Item Master' interface in the Sand Planet system. At the top, there's a navigation bar with 'SAND PLANET' and links for 'Project Management', 'My Tasks' (with a red notification icon), 'Sites', and 'Procurement'. The user is logged in as 'Hassan Rasheed · HO PURCHASING' with a 'Sign out' button. Below the navigation bar, there are tabs for 'Purchasing Dashboard', 'Items' (selected), 'Item Categories', and 'Suppliers'. The 'Item Master' section features a search bar labeled 'Search description / code / category...'. Below the search bar, there are input fields for 'Description (size, grade, spec, brand)', 'Unit...' (a dropdown), 'Category...' (a dropdown), and 'Brand', followed by an 'Add item' button. The main content is a table listing 12 items, each with a 'Code', 'Description', 'Unit', 'Category', and 'Brand'. Each item has a 'Discontinue' button next to it.

Code	Description	Unit	Category	Brand
ITM-00001	Cement OPC 50kg bag	Bag	Civil	Discontinue
ITM-00002	Rebar B500 12mm	Kg	Civil	Discontinue
ITM-00003	Rebar B500 10mm	Kg	Civil	Discontinue
ITM-00004	Hollow block 8"	Nos	Civil	Discontinue
ITM-00005	River sand	m³	Civil	Discontinue
ITM-00006	Aggregate 20mm	m³	Civil	Discontinue
ITM-00007	Waterproofing membrane 1.5mm	Roll	Finishes	Discontinue
ITM-00008	Tile adhesive 20kg	Bag	Finishes	Discontinue
ITM-00009	Porcelain tile 600×600 Grade A	m²	Finishes	Discontinue
ITM-00010	PVC pressure pipe 63mm	m	MEP	Discontinue
ITM-00011	PPR pipe 25mm	m	MEP	Discontinue
ITM-00012	Pool circulation pump 2HP	Nos	Pool	Discontinue

The company-wide item catalogue, owned by Head Office Purchasing.

Registers

Every document type has a register, and every register builds itself. Filter by date or status; export any register to Excel or PDF. The DPR & TWS register lists every working day, so a day with no report shows as a visible gap — Fridays are off by default and never flagged. Head Office holds master registers across all sites, plus the Pending Items Log: every item that missed a boat, why, and which boat it's going on next. It clears itself when the item ships.

Petty cash

Each site holds a fixed float with a named custodian — the Site Admin.

Recording spending. Date, amount, what it was for, which cost head, and a photo of the receipt. No receipt? Say so and give the reason. Anything above the per-transaction cap is blocked — that spending goes through a PYR instead. The PM approves the entries in a batch, weekly or at replenishment.

SAND PLANET Project Management Aishath Reena · SITE ADMIN [Sign out](#)

Petty Cash — SJR

Cash in hand **MVR 15,880.00**

Imprest MVR 20,000.00 · trigger 30% (MVR 6,000.00)
Custodian Aishath Reena · cap MVR 1,500.00 / txn
Cycle 1 · [OPEN](#)

[+ Expense](#) [Reconcile](#) [← Back](#)

Date	Amount	Cost head	Payee / purpose	Receipt	Status
2026-07-10	1,450.00	Site Overheads	Fuel for site generator · Fuel for site generator		RECORDED
2026-07-10	1,180.00	Site Overheads	Hardware sundries — fixings · Hardware sundries — fixings		RECORDED
2026-07-10	640.00	Site Overheads	Drinking water (bulk) · Drinking water (bulk)		RECORDED
2026-07-10	850.00	Site Overheads	Ferry tickets — crew rotation · Ferry tickets — crew rotation		RECORDED

The site's petty-cash float, its entries and running balance.

Getting the money back. When the balance runs low, raise a replenishment request. Planet fills in the amount and attaches the whole expense schedule with receipts — you type nothing. It travels the normal PYR route, and when Finance pays it the float restores itself and the cycle closes. **Counting.** Once a month, count the cash and enter what you counted; Planet compares it to what it thinks you should have and records any difference with your explanation.

Timesheets and payroll

Employees (HR / Payroll). Name, passport, nationality, job category, basic pay, work permit and expiry. Basic pay and passport numbers are visible only to HR and the Administrator — never to site staff.

Daily attendance (Site Admin). One screen, the whole crew, times pre-filled from the site's working hours. Change the exceptions, mark absences and leave, enter overtime.

SAND PLANET Project Management Ibrahim Naseer · SITE ENGINEER [Sign out](#)

Attendance — SJR 10-07-2026 [Close](#)

🔒 This month is signed off and locked. Corrections require an HO HR reopen.

Emp No	Name	Category	In	Out	Remark	OT req (h)	OT approved
EMP-0001	Kumara Perera	Mason	07:00	18:00	PRESENT	0	—
EMP-0002	Rahim Uddin	Steel Fixer/Bar Bender	07:00	18:00	PRESENT	0	—
EMP-0003	Suresh Nair	Plumber	07:00	18:00	PRESENT	0	—
EMP-0004	Anil Chowdhury	Carpenter	07:00	18:00	PRESENT	0	—
EMP-0005	Prakash Thapa	Electrician	07:00	18:00	PRESENT	0	—
EMP-0006	Mohamed Faisal	Foreman	07:00	18:00	PRESENT	0	—

Daily attendance — the whole crew on one screen, times pre-filled.

Overtime approval (PM). Overtime counts only once the PM approves it; unapproved hours are visible but can never reach payroll. **Month close.** The PM signs off and the site's timesheet locks. When every site is locked, HR exports the payroll figures. A locked month reopens only through HR, with a reason, recorded.

SAND PLANET

Project Management

Sites

People

Mariyam Shifa · HO HR

Sign out

HR Dashboard

Employees

Payroll

Staff Cost

Payroll — 2026-07

July 2026

All sites (consolidated)

Download Excel

OT multiplier × 1.25 · hourly rate = basic ÷ 240 (company parameters)

Emp No	Name	Site(s)	Days	Absences	Hours	OT (appr.)	Basic	OT Amount	Gross
EMP-0001	Kumara Perera	SJR	6	0	66	2	9,600	100	9,700
EMP-0002	Rahim Uddin	SJR	6	0	66	2	9,000	93.75	9,093.75
EMP-0003	Suresh Nair	SJR	6	0	66	2	10,200	106.25	10,306.25
EMP-0004	Anil Chowdhury	SJR	6	0	66	0	9,300	0	9,300
EMP-0005	Prakash Thapa	SJR	6	0	66	0	10,500	0	10,500
EMP-0006	Mohamed Faisal	SJR	6	0	66	0	14,000	0	14,000
Total gross									MVR 62,900


The payroll export — gross pay built from approved hours only.

Money: how a payment actually travels

Worth understanding, because it explains why things wait where they wait.

- 1 You raise a PR or PYR.
- 2 Your PM approves it (PYR only).
- 3 The Director approves it — this is commercial approval: *should we buy this?*
- 4 A signatory — one of the two executive directors — authorises it. This is the moment the money is committed to the project. Either director can do it. They may also send it back for review, with a reason, and nothing is committed.
- 5 Finance pays it and records the transfer or cheque reference. Finance does not authorise; Finance disburses.

The person approving spending is never the person releasing it. A credit purchase is authorised now and paid later on terms — it appears in Finance's payables until settled.

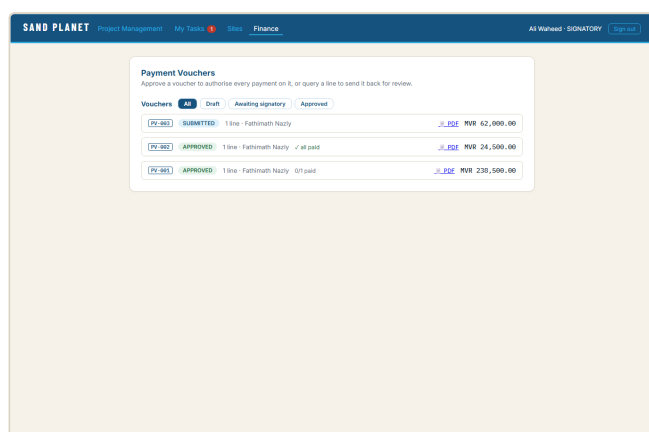

The signatory's queue — each request whole on one screen: authorise, or return.

SANDPLANET		PAYMENT VOUCHER					
Voucher No. PV-001		Date 10.07.2026		Status APPROVED			
Prepared By Fathimath Nazki							
No.	Requisition	Site	Payee	Purpose	Cost Head	Amount (BWP)	Payment Ref
1	PR-001	SAR	Alsa Building Supplies, Male' Hardware Pvt Ltd	Procurement	Materials	238,500.00	TRF-30021
Total Authorised (BWP)						238,500.00	
Prepared / Submitted By — Finance				Authorised By — Signatory (Executive Director)			
Fathimath Nazki — FINANCE — 100726 08:42 — approved electronically via Sand Planet Project Management App				Ali Waheed — SIGNATORY — 100726 08:42 — approved electronically via Sand Planet Project Management App			
A signed line is returned to its issuer and is not authorised on this voucher. Disbursement is made against each requisition; the Payment Ref is the transfer / cheque number recorded by Finance on release. Bank release requires the two authorised signatories per the company mandate.							
Sand Planet Pvt Ltd TIN 10028602703 PAYMENT VOUCHER http://sandplanet.mv Via: Moovache app / Mobile							

The authorised Payment Voucher that releases the requisitions.

Projects and cost

A site in Planet is a project: created when the contract is awarded, closed when the work is done. It holds scope, contract value, dates, client and consultant contacts, and its assigned PM — and that assignment routes every approval on that site. Projects run Awarded → Active → On Hold → Closed. Awarded lets you buy before the site opens; Closed stops new documents but keeps everything readable forever.

The screenshot shows the SAND PLANET Project Management interface. The top navigation bar includes 'SAND PLANET', 'Project Management', 'My Tasks' (with a red notification badge '2'), and 'Sites'. The user 'Mohamed Shazin · PM' is logged in, with a 'Sign out' button.

The main content area displays the project workspace for 'Proposed Construction of 17 Swimming Pools' (ID: POOLS17). The project status is 'ACTIVE' (green), and the location is 'SJR'. A 'Programme PDF' link is available, along with a 'Back' button.

Below the project title, there are tabs for 'Overview' (selected), 'Programme', 'Manpower plan', 'Documents', 'BOM - Phase B', 'Budget - later', and 'Tender - later'.

The 'Overview' tab shows four key metrics:

- 0% Programme progress**: behind — 35% of time elapsed
- 11 Activities**: in the programme
- Manpower (last DPR)**: reported at site
- 18,500,000 Contract value**: MVR

Below these metrics is a table with project details:

Project PM	Mohamed Shazin
LOA date	2026-04-10
Start date	2026-04-22
Planned finish	2026-12-05
Actual completion	—
BOQ ref	—
Scope	17 pools, plant rooms, MEP and finishes across the resort.
Planned manpower	179 across 4 categories

A note at the bottom states: 'Project details are edited under Admin → Site Setup.'

The project workspace — scope, programme and progress in one place.

Cost tracking — three numbers, three meanings

Every purchase, payment, petty-cash entry and month of staff cost flows into the project automatically. You see three numbers, and they mean different things:

- **Committed** — authorised and binding, not yet paid.
- **Incurred** — what the project has actually consumed. Materials count when they land on site, not when they're ordered.
- **Paid** — cash out of the company.

Each cost carries a cost head — Materials, Labour & Staff, Subcontract, Plant & Equipment, Transport & Freight, Site Overheads, Permits & Fees, Other — so you can see where the money went, and click any figure to reach the document behind it. The Projects page shows percentage of contract consumed beside percentage of duration elapsed; if the first runs ahead of the second, that project needs attention.

SAND PLANETProject ManagementMy TasksSitesProcurementPeopleAdminAhmad Zaki · DIRECTORSign out

My TasksPortfolioProject Cost

Project cost control

Site	Contract	Committed	Incurred	Paid	Consumed vs elapsed
SJR Simso Jari	15,500,000.00	263,000.00	325,980.00	121,000.00	1.8% vs 14.8%
Portfolio	15,500,000.00	263,000.00	325,980.00	121,000.00	

Committed / Incurred / Paid per project, with consumed-vs-elapsed.

SAND PLANETProject ManagementMy TasksSitesProcurementPeopleAdminAhmad Zaki · DIRECTORSign out

My TasksPortfolioProject Cost

Portfolio

1Active projects
across all sites

0On hold
none

1Needing attention
progress well behind programme

Project	Site	PM	Value (MVR)	Finish	Time	Progress	Open	Health
PROJ327 Proposed Construction of 17 Swimming Pools	SJR	Mohamed Shazin	15,500,000	2026-12-05	34.0%	0%	0	Attention

The portfolio — every project's value, cost and whether it's on track.

Cost figures are confidential: Head Office, the Administrator, Senior Management, and the project's own PM. Site users see no cost data — only their own petty-cash balance and the payment requests they raise.



CONSTRUCTION PROGRAMME

Project	Proposed Construction of 17 Swimming Pools (POOLS17)	Client	Soneva Jani Resort
Site	Soneva Jani (SJR)	LOA / Start / Finish	10.04.2026 · 22.04.2026 · 05.12.2026
Prepared	10.07.2026	BOQ Ref	—

1. PROGRAMME OF WORKS

Activity	Days	Start	Finish	Apr 26	May 26	Jun 26	Jul 26	Aug 26	Sep 26	Oct 26	Nov 26	Dec 26
PROPOSED CONSTRUCTION OF 17 NOS SWIMMING POOLS	233	17/04/26	05/12/26									
CONTRACT MILESTONES	228	22/04/26	05/12/26									
◆ Start Date in Local Island	0	22/04/26	22/04/26									
MOBILISATION & SITE SETUP	14	23/04/26	07/05/26									
POOL SHELL — POOLS 1-6	60	08/05/26	07/07/26									
Excavation & Formwork	20	08/05/26	28/05/26									
Footings & Wall Concreting	25	29/05/26	22/06/26									
Waterproofing & Screed	15	23/06/26	07/07/26									
POOL FINISHES — POOLS 1-6	45	08/07/26	21/08/26									
MEP & PLANT ROOM	50	08/07/26	26/08/26									
◆ HANDOVER — PHASE 1	0	21/08/26	21/08/26									

Solid fill inside a bar shows progress to date. ◆ = milestone.

The project programme, issued to the client with the award.

International procurement · later phase

Arriving in a later phase. The screens below are described here so the whole picture is in one place, but they are not yet part of Planet — you will not find them in the app today.

Head Office manages all imports, but your project's requirement is tracked at project level and appears on your dashboard.


- **PMR — Project Material Requirement.** How a project asks for imported material. Raised by the project team, reviewed by HO project staff, sized by the Director — whose order quantity may be much larger than you asked for, because suppliers impose minimum orders. Your share is reserved to your project; the surplus becomes general company stock.
- **IPR — International Purchase Requisition.** The overseas order. Becomes the purchase order once a signatory authorises it.
- **IRN — Import Receipt Note.** The count against the packing list when a shipment clears customs in Malé.
- **SIN — Store Issue Note.** How goods leave the Head Office store for a site.

Then you watch it move on your own dashboard:


sized → ordered → advance paid → in production → shipped → arrived Malé → clearing → on manifest → received. Imported goods only become project cost when they land on your site — valued at their true landed cost, including freight, duty and clearing, not just the invoice price.

On your phone, and small things worth knowing

Planet is built for the site as much as the office. On a phone it stays legible and one-handed: today's obligations first, the camera one tap away for DPR photos, drafts held safely through a dropped signal.



The site dashboard on a phone.



A DPR reviewed from the field.

- **Notifications** tell you when something needs you — a document to approve, a boat coming, a shortage reported.
- **Everything is recorded.** Who created, approved, changed, returned or voided anything, and exactly when. Nothing is deleted.
- **Conventions.** Dates are dd/mm/yy. Times are 24-hour. Money is MVR unless a supplier is overseas.

If something goes wrong

Wrong figures on an issued document? Don't fight it. Revise it (MAR, MR), raise a new one linked to the old (IR), or ask your Administrator to void it with a reason. The register will show exactly what happened — which is the point. Questions go to your Administrator.
